PIV BURSA NEW PAINT LINE
PRELIMINARY TIME SCHEDULE

G. CHARLON
March 06 2006
rev 4
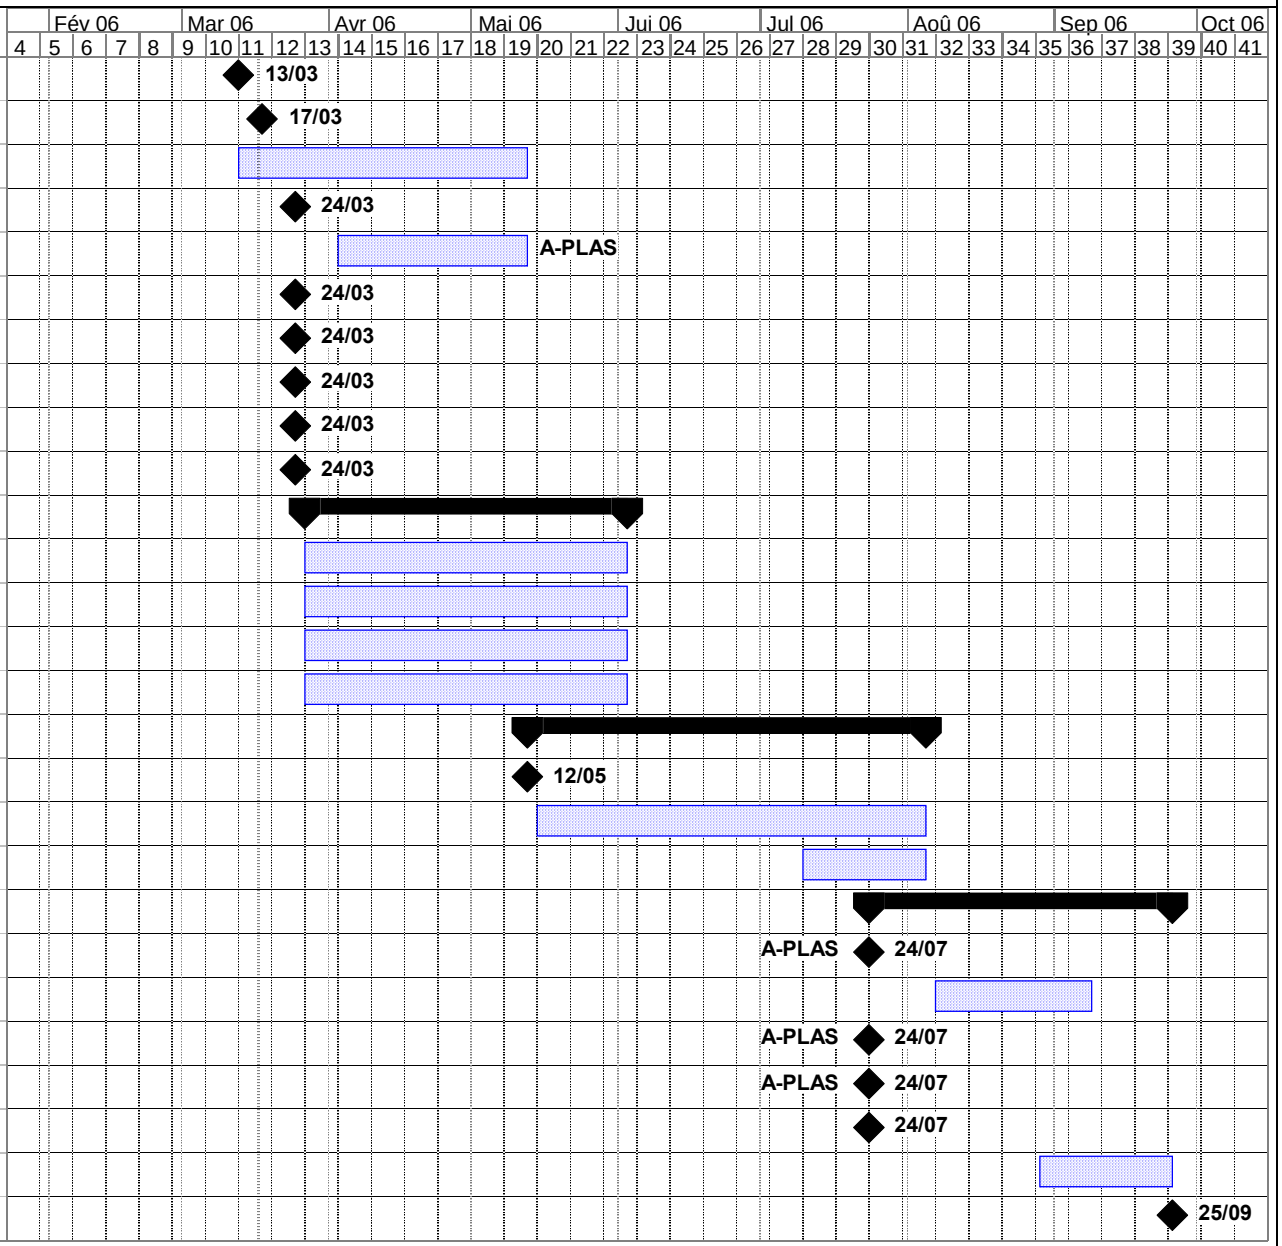
N°	Nom de la tâche	Prédécesse	Durée
1	PURCHASE ORDER		0 jour
2	KICK OFF MEETING	1FD+1 sm	0 jour
3	ENGINEERING	1	9 sms
4	FIRST ENGINEERING REVUE	3DD+2 sms	0 jour
5	CONCRETE WORK	4FD+1 sm	6 sms
6	**MAIN SUPPLYING ORDER**		**0 jour**
7	CONVEYOR	4	0 jour
8	FANS	4	0 jour
9	BURNER	4	0 jour
10	ELECTRICAL AND CONTROL	4	0 jour
11	**MANUFACTURING**		**50 jours**
12	BOOTHS	4	10 sms
13	OVEN	4	10 sms
14	AIR UNITS	4	10 sms
15	DUCTING	4	10 sms
16	**INSTALLATION**		**60 jours**
17	SITE OPENING	5	0 sm
18	PAINT LINE	5	12 sms
19	CONVEYOR	5FD+8 sms	4 sms
20	**START-UP**	**18FD-2 sms**	**46 jours**
21	ENERY AVALIABILITY		0 jour
22	PAINT LINE START-UP	18	5 sms
23	GIGS AND MATS		0 jour
24	RINSING PRODUCTS		0 jour
25	PAINT PRODUCTS		0 jour
26	PAINT APPLICATION	22FD-9 jour	4 sms
27	PRODUCTION	26	0 jour
